

# TECHNOLOGY BOND UPDATE



Kyle Berger  
Chief Technology Officer

March 31, 2015



# TECHNOLOGY BOND UPDATE

March 31, 2015

## *Technology Bond Overview*

Technology Bond Total : \$17,665,277

Projects :

- ▶ Upgrade District wide Network
- ▶ Replace District phone system
- ▶ Replace Data Cabling ( Hardin , Daniel, Brandenburg, Kennemer)
- ▶ Classroom Technology Upgrades (District Wide)
- ▶ Community Wi-Fi
- ▶ Future Technology



# TECHNOLOGY BOND UPDATE

March 31, 2015

## District Wide Network Upgrade Timelines

Network assessment :	Summer 2014	Complete
Network bid package released:	January 2015	Complete
Network bids received and Vendor Selected :	February 2015	Complete
Vendor site walk and pre design meetings:	February 2015	Complete
Po issued for network project:	April 1, 2015	In Progress
Network replacement starts :	June 9, 2015	
Network replacement completion:	August 7, 2015	



# TECHNOLOGY BOND UPDATE

March 31, 2015

## District Phone Upgrade Timelines

Phone assessment :	Summer 2014	Complete
Phone bid package released:	January 2015	Complete
Phone bids received and Vendor Selected :	February 2015	Complete
Vendor site walk and pre design meetings:	February 2015	Complete
Po issued for phone project:	April 1, 2015	In Progress
Phone replacement starts :	June 9, 2015	
Phone replacement completion:	July 24, 2015	



# TECHNOLOGY BOND UPDATE

March 31, 2015

## Data Cabling Replacement Timelines

Daniel Data cable replacement:	Summer 2015
Hardin Data cable replacement:	Summer 2015
Kennemer Data cable replacement:	Summer 2016
Brandenburg Data cable replacement:	Pending Renovation Schedule



# TECHNOLOGY BOND UPDATE

March 31, 2015

## Classroom Technology Timelines

Classroom technology physical assessment:	November- December 2014	Completed
Student focus groups (5 groups –(k-4,5-6,7-8,9-12):	January – March 2015	Completed
Teacher focus groups (k-4,5-6,7-8,9-12 / Art /Band / Music / Special Ed , Athletics) :	January – April 2015	In progress
District level instructional focus group:	March 2015	Completed
Plan finalized and phasing established:	April - May 2015	In progress
Bids released for phase 1:	May 2015	
Orders placed for phase 1:	June 2015	
Phase 1 completion :	Oct 2015	
Phase 2 orders placed:	May 2016	
Phase 2 completion:	Sept 2016	
Phase 3 orders placed: *	May 2017*	
Phase 3 completion:*	Sept 2017*	

*\*if needed*



# TECHNOLOGY BOND UPDATE



March 31, 2015

## Community Wi-Fi

- Joint meetings with City of Duncanville for park location placement have been completed
- Possible site locations have been mapped throughout school district
- Kiosk design and network framework is in progress

In the coming months:

- Meeting with local chambers and other locations to begin site selection
- Order placed for 40 kiosk units

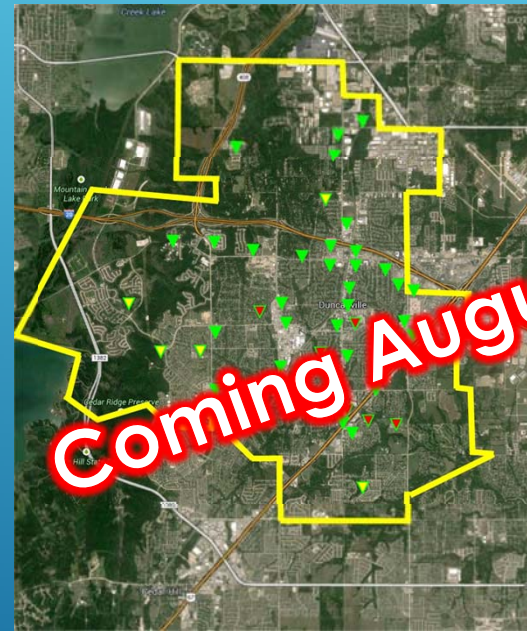



# TECHNOLOGY BOND UPDATE

March 31, 2015

Approximate expenditures and completion by September 2015

